

Project: 0201 CS Baseline 20021106 Date: Sun 11/10/02	Critical		Baseline		External Tasks	
	Critical Split		Baseline Split		Project Summary	
	Critical Progress		Baseline Milestone		External Milestone	
	Task		Milestone		Deadline	
	Split		Summary Progress			
	Task Progress		Summary			


ID	Task Name	Duration	Start	Finish	November 2002	December 2002	January 2003
					06		
29	Tape/Texture	10 d	Wed 01/29/03	Tue 02/11/03			
30	Bath Cer Flr Tile	5 d	Wed 02/12/03	Tue 02/18/03			
31	Int Paint	10 d	Wed 02/12/03	Tue 02/25/03			
32	Toil Part/Acc	5 d	Wed 02/26/03	Tue 03/04/03			
33	Cabs/C-Tops	10 d	Wed 02/26/03	Tue 03/11/03			
34	MEP Finishes	20 d	Wed 02/26/03	Tue 03/25/03			
35	T-Bar Ceilings	10 d	Wed 02/26/03	Tue 03/11/03			
36	Drs/Fms/Hdwe	20 d	Wed 02/26/03	Tue 03/25/03			
37	Mouldings	10 d	Wed 02/26/03	Tue 03/11/03			
38	Flooring	10 d	Wed 03/26/03	Tue 04/08/03			
39	Exterior	60 d	Wed 11/27/02	Tue 02/18/03			
40	Ext Wall Framing	10 d	Wed 11/27/02	Tue 12/10/02			
41	Lath Exterior	10 d	Wed 12/25/02	Tue 01/07/03			
42	Windows	10 d	Wed 01/08/03	Tue 01/21/03			
43	Plaster	10 d	Wed 01/22/03	Tue 02/04/03			
44	Ext Paint	5 d	Wed 02/05/03	Tue 02/11/03			
45	Ext Finishes/Fixtures	5 d	Wed 02/12/03	Tue 02/18/03			
46	2nd Floor	100 d	Thu 12/12/02	Wed 04/30/03			
47	Interior	100 d	Thu 12/12/02	Wed 04/30/03			
48	Int Wall Framing	20 d	Thu 12/12/02	Wed 01/08/03			
49	MEP Rough-In	20 d	Thu 01/09/03	Wed 02/05/03			
50	Gyp Bd Side 1	7 d	Thu 01/09/03	Fri 01/17/03			
51	Insulate	3 d	Mon 02/03/03	Wed 02/05/03			
52	Gyp Bd Side 2/Dr Fms	5 d	Thu 02/06/03	Wed 02/12/03			
53	Gypcrete	5 d	Thu 02/13/03	Wed 02/19/03			
54	Tape/Texture	10 d	Thu 02/20/03	Wed 03/05/03			
55	Bath Cer Flr Tile	5 d	Thu 03/06/03	Wed 03/12/03			
56	Int Paint	10 d	Thu 03/06/03	Wed 03/19/03			

Project: 0201 CS Baseline 20021106 Date: Sun 11/10/02	Critical		Baseline		External Tasks	
	Critical Split		Baseline Split		Project Summary	
	Critical Progress		Baseline Milestone		External Milestone	
	Task		Milestone		Deadline	
	Split		Summary Progress			
	Task Progress		Summary			

ID	Task Name	Duration	Start	Finish	November 2002	December 2002	January 2
					06		
57	Toil Part/Acc	5 d	Thu 03/20/03	Wed 03/26/03			
58	Cabs/C-Tops	10 d	Thu 03/20/03	Wed 04/02/03			
59	MEP Finishes	20 d	Thu 03/20/03	Wed 04/16/03			
60	T-Bar Ceilings	10 d	Thu 03/20/03	Wed 04/02/03			
61	Drs/Fms/Hdwe	20 d	Thu 03/20/03	Wed 04/16/03			
62	Mouldings	10 d	Thu 03/20/03	Wed 04/02/03			
63	Flooring	10 d	Thu 04/17/03	Wed 04/30/03			
64	Exterior	60 d	Thu 12/12/02	Wed 03/05/03			
65	Ext Wall Frmng	10 d	Thu 12/12/02	Wed 12/25/02			
66	Lath Exterior	10 d	Thu 01/09/03	Wed 01/22/03			
67	Windows	10 d	Thu 01/23/03	Wed 02/05/03			
68	Plaster	10 d	Thu 02/06/03	Wed 02/19/03			
69	Ext Paint	5 d	Thu 02/20/03	Wed 02/26/03			
70	Ext Finishes/Fixtures	5 d	Thu 02/27/03	Wed 03/05/03			
71	Bldg Punch	10 d	Thu 05/01/03	Wed 05/14/03			
72	Sitework	121 d	Wed 11/06/02	Wed 04/23/03			
73	North Lot	15 d	Wed 11/20/02	Tue 12/10/02			
74	Demo/Fine Grade	2 d	Wed 11/20/02	Thu 11/21/02			
75	Utilities	3 d	Fri 11/22/02	Tue 11/26/02			
76	Irrig	3 d	Fri 11/22/02	Tue 11/26/02			
77	C/G/S	5 d	Wed 11/27/02	Tue 12/03/02			
78	AC/Grass Pave	4 d	Wed 12/04/02	Mon 12/09/02			
79	Misc Site Furn	5 d	Wed 12/04/02	Tue 12/10/02			
80	Planting	5 d	Wed 12/04/02	Tue 12/10/02			
81	Courtyard	98 d	Wed 11/06/02	Fri 03/21/03			
82	Block Walls	8 d	Wed 11/06/02	Fri 11/15/02			
83	Fine Grading	2 d	Thu 02/20/03	Fri 02/21/03			
84	Utilities	5 d	Mon 02/24/03	Fri 02/28/03			

Project: 0201 CS Baseline 20021106 Date: Sun 11/10/02	Critical		Baseline		External Tasks	
	Critical Split		Baseline Split		Project Summary	
	Critical Progress		Baseline Milestone		External Milestone	
	Task		Milestone		Deadline	
	Split		Summary Progress			
	Task Progress		Summary			

ID	Task Name	Duration	Start	Finish	November 2002	December 2002	January 2
					06		
85	Irrigation	7 d	Mon 02/24/03	Tue 03/04/03			
86	Cisterns	5 d	Mon 03/03/03	Fri 03/07/03			
87	Flatwork	10 d	Mon 03/03/03	Fri 03/14/03			
88	Misc Site Furn	5 d	Mon 03/17/03	Fri 03/21/03			
89	Planting	5 d	Mon 03/17/03	Fri 03/21/03			
90	SouthEast Lot	20 d	Thu 02/20/03	Wed 03/19/03			
91	Demo/Fine Grade	3 d	Thu 02/20/03	Mon 02/24/03			
92	Utilities	2 d	Tue 02/25/03	Wed 02/26/03			
93	Irrig	3 d	Tue 02/25/03	Thu 02/27/03			
94	C/G/S	5 d	Thu 02/27/03	Wed 03/05/03			
95	AC/Grass Pave	5 d	Thu 03/06/03	Wed 03/12/03			
96	Misc Site Furn	2 d	Thu 03/06/03	Fri 03/07/03			
97	Planting	5 d	Thu 03/13/03	Wed 03/19/03			
98	SouthWest Lot	40 d	Wed 11/06/02	Tue 12/31/02			
99	Haul-off Spoils	3 d	Wed 11/06/02	Fri 11/08/02			
100	Demo/Fine Grade	3 d	Mon 11/11/02	Wed 11/13/02			
101	Utilities	7 d	Thu 11/14/02	Fri 11/22/02			
102	Irrig	5 d	Thu 11/14/02	Wed 11/20/02			
103	Walls/Stairs	10 d	Mon 11/25/02	Fri 12/06/02			
104	C/G/S	10 d	Mon 12/09/02	Fri 12/20/02			
105	AC/Grass Pave	2 d	Mon 12/23/02	Tue 12/24/02			
106	Misc Site Furn	5 d	Mon 12/23/02	Fri 12/27/02			
107	Planting	5 d	Wed 12/25/02	Tue 12/31/02			
108	Shade Structure	35 d	Thu 02/20/03	Wed 04/09/03			
109	Drill Holes	5 d	Thu 02/20/03	Wed 02/26/03			
110	Set Posts	5 d	Thu 02/27/03	Wed 03/05/03			
111	Hardware	10 d	Thu 03/06/03	Wed 03/19/03			
112	Trellises	10 d	Thu 03/06/03	Wed 03/19/03			

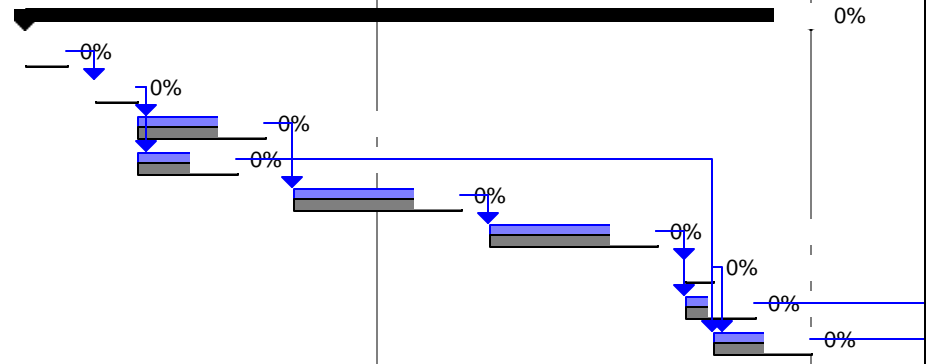


Project: 0201 CS Baseline 20021106 Date: Sun 11/10/02	Critical		Baseline		External Tasks	
	Critical Split		Baseline Split		Project Summary	
	Critical Progress		Baseline Milestone		External Milestone	
	Task		Milestone		Deadline	
	Split		Summary Progress			
	Task Progress		Summary			

ID	Task Name	Duration	Start	Finish	November 2002	December 2002	January 2003
					06		
113	Paint Poles	5 d	Thu 03/06/03	Wed 03/12/03			
114	Paint Hdwe/Trellises	5 d	Thu 03/20/03	Wed 03/26/03			
115	Fabric/Mesh	10 d	Thu 03/27/03	Wed 04/09/03			
116	Site Punchlist	10 d	Thu 04/10/03	Wed 04/23/03			
117	Completion	0 d	Wed 11/06/02	Wed 11/06/02	11/06		




Project: 0201 CS Baseline 20021106 Date: Sun 11/10/02	Critical		Baseline		External Tasks	
	Critical Split		Baseline Split		Project Summary	
	Critical Progress		Baseline Milestone		External Milestone	
	Task		Milestone		Deadline	
	Split		Summary Progress			
	Task Progress		Summary			

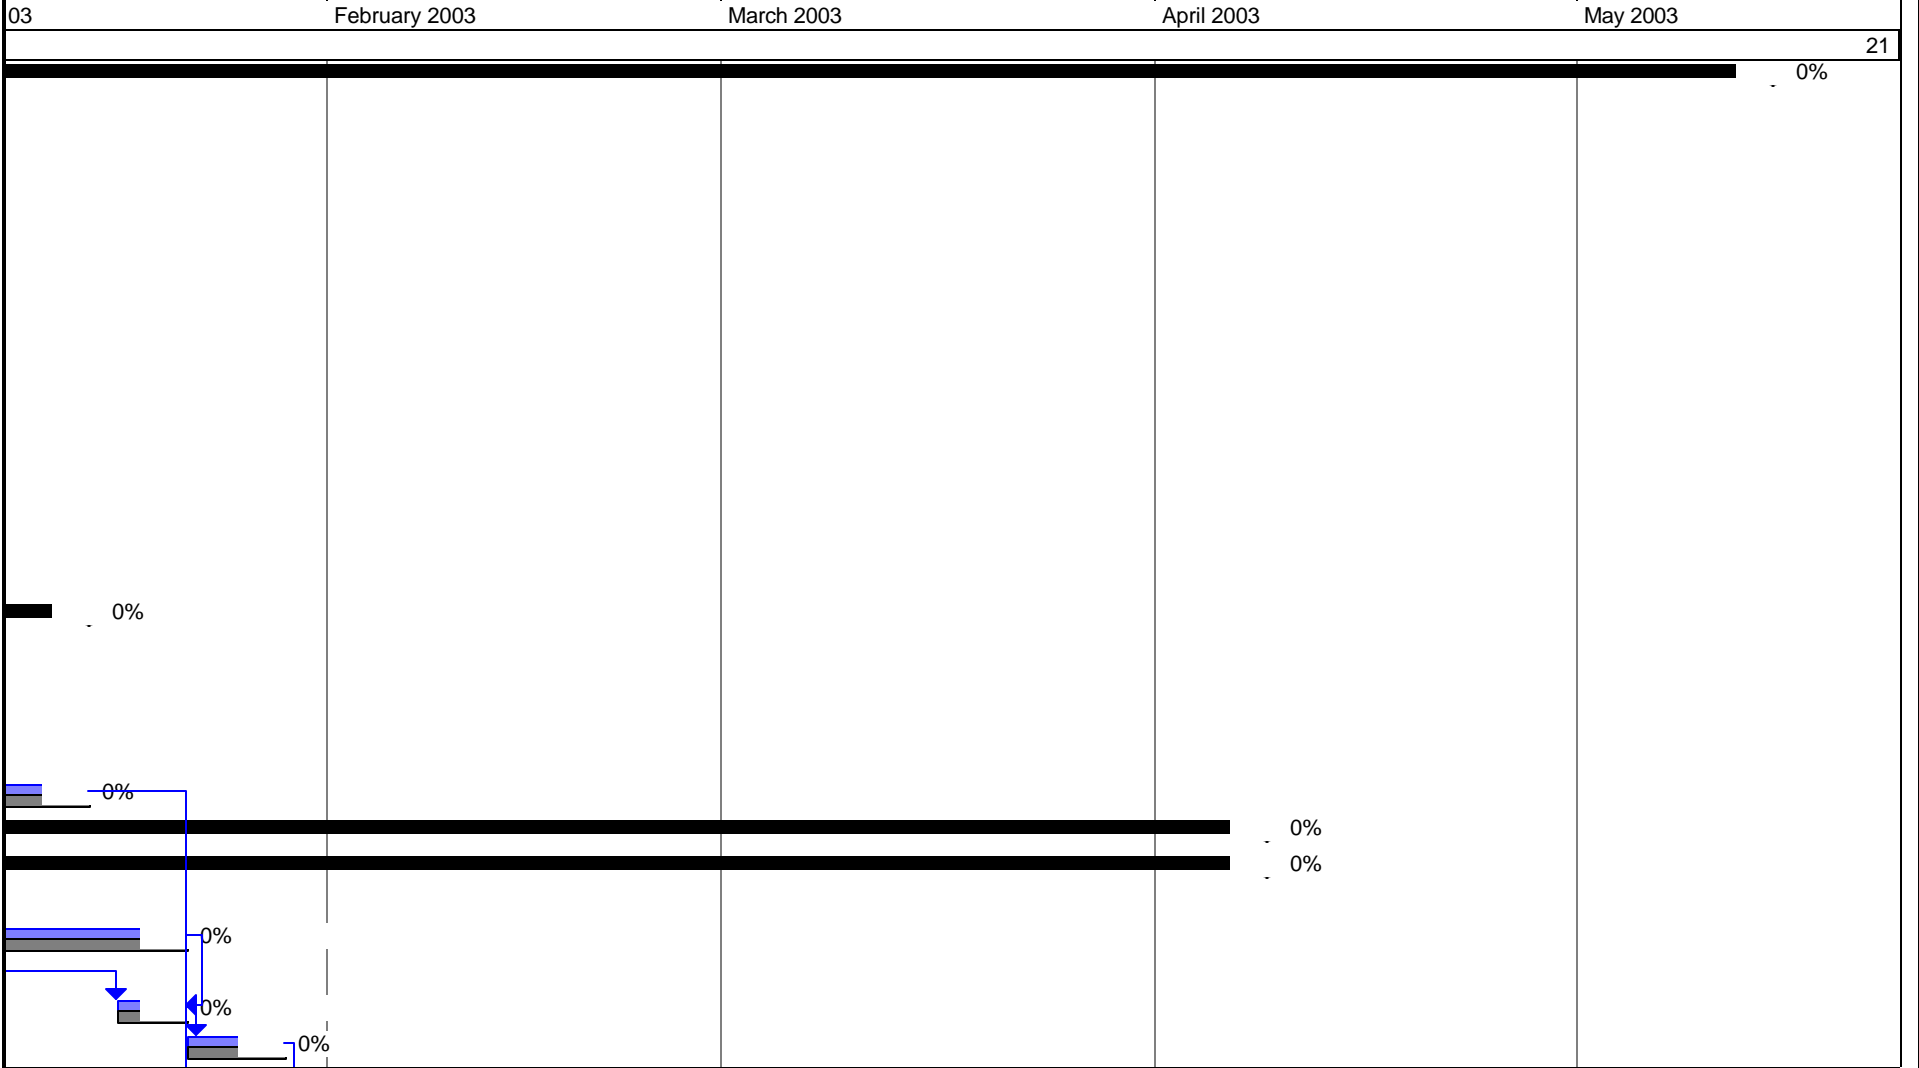


Project: 0201 CS Baseline 20021106
Date: Sun 11/10/02

Critical		Baseline		External Tasks	
Critical Split		Baseline Split		Project Summary	
Critical Progress		Baseline Milestone		External Milestone	
Task		Milestone		Deadline	
Split		Summary Progress			
Task Progress		Summary			

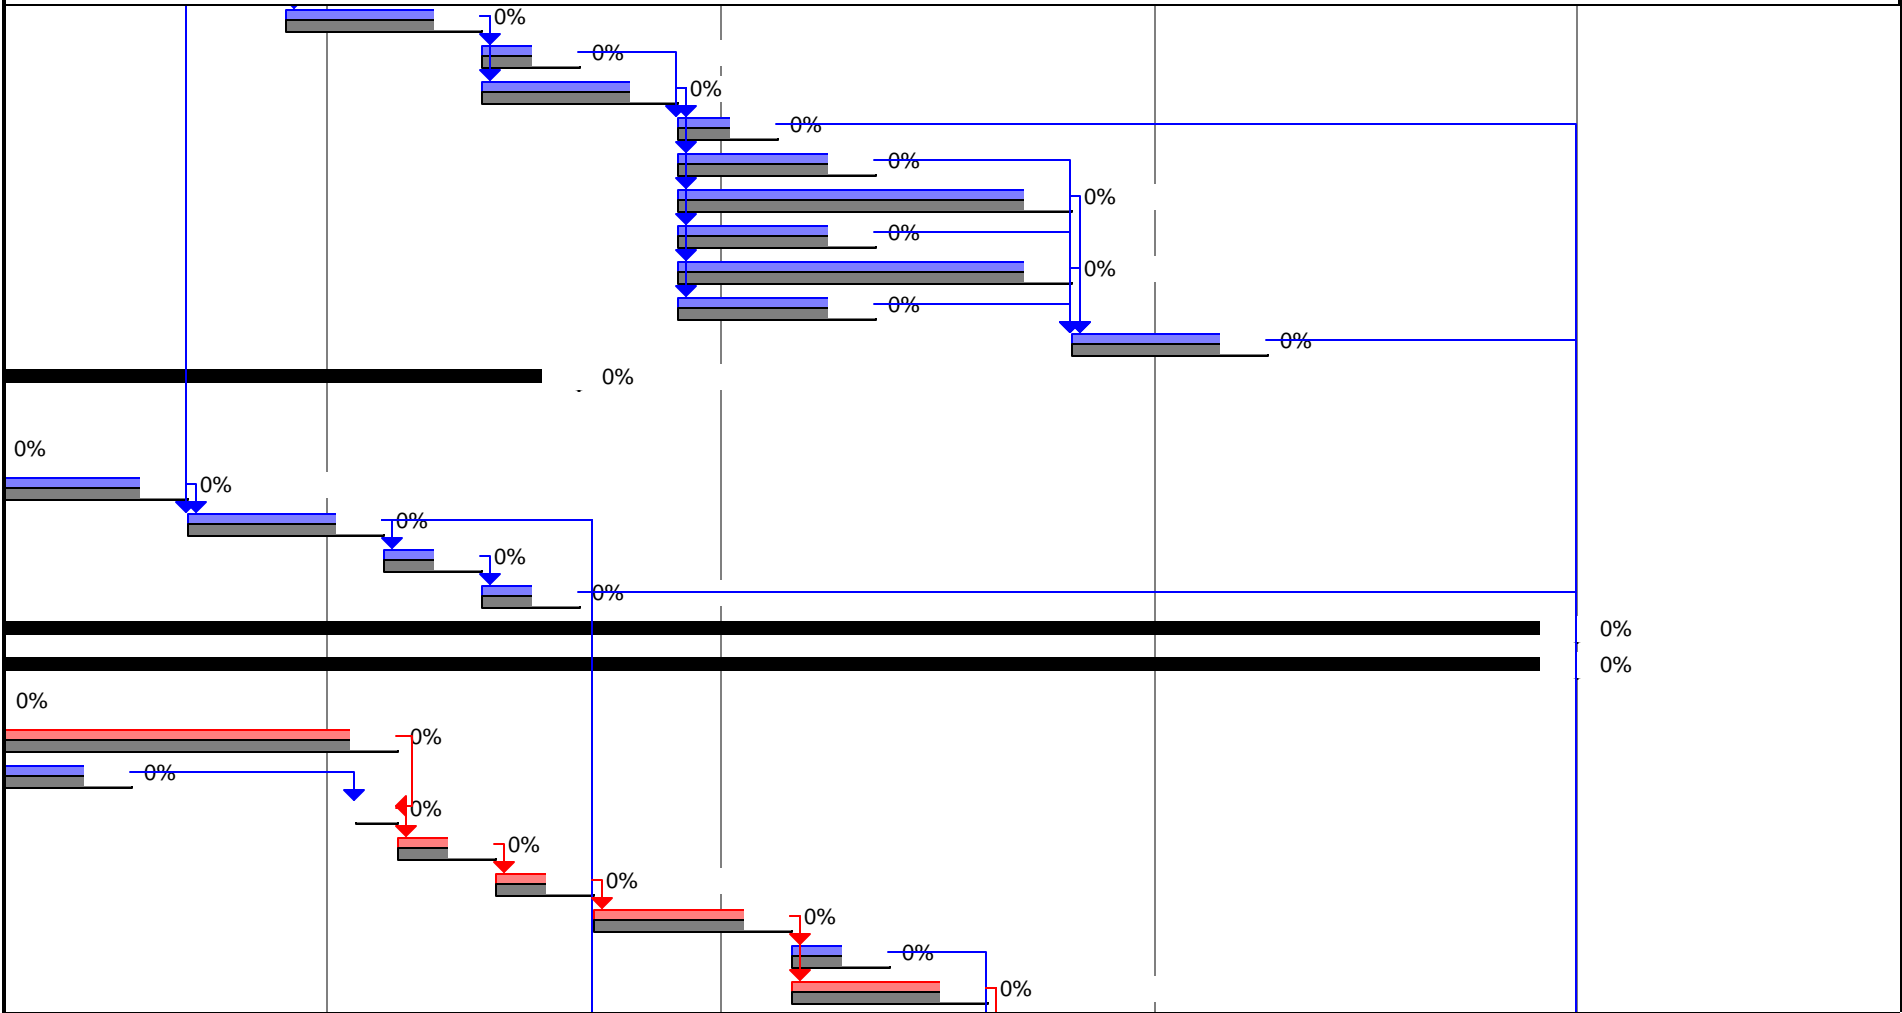


Project: 0201 CS Baseline 20021106
 Date: Sun 11/10/02

Critical		Baseline		External Tasks	
Critical Split		Baseline Split		Project Summary	
Critical Progress		Baseline Milestone		External Milestone	
Task		Milestone		Deadline	
Split		Summary Progress			
Task Progress		Summary			

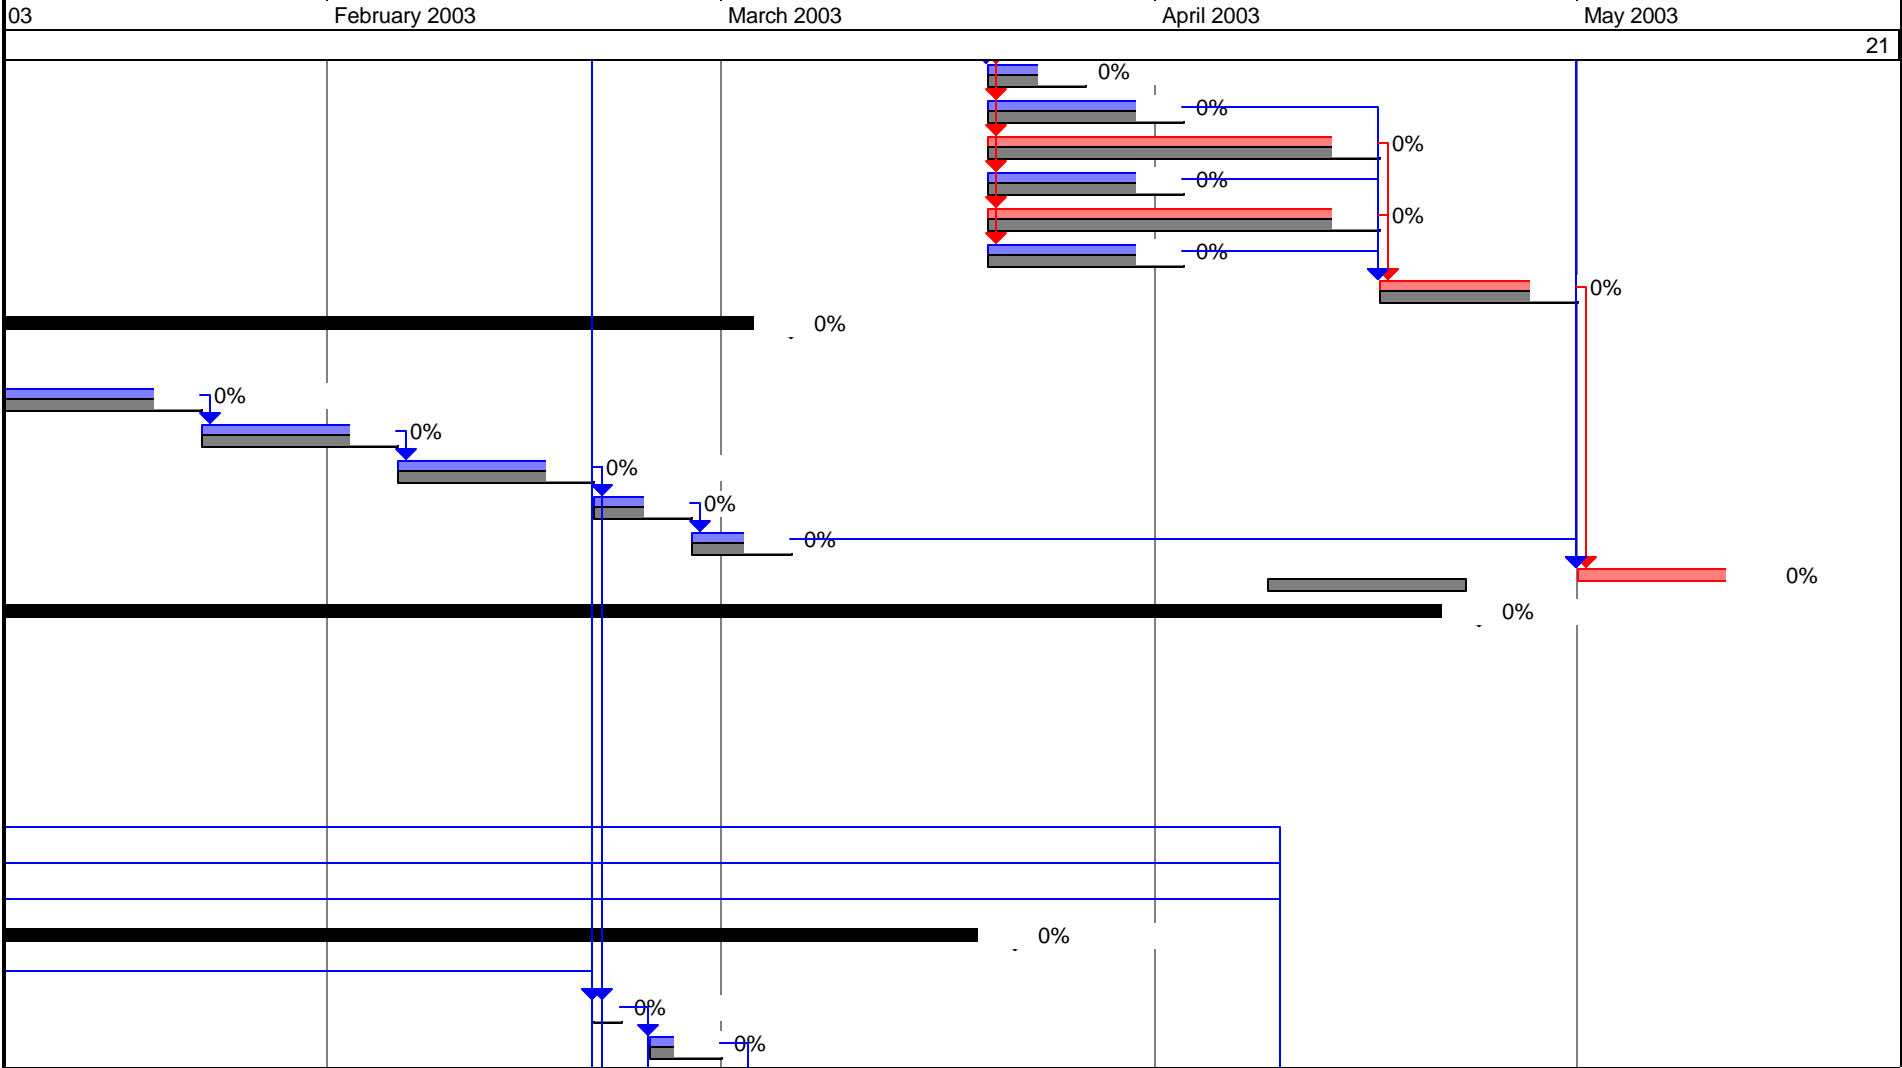


Project: 0201 CS Baseline 20021106
Date: Sun 11/10/02

Critical		Baseline		External Tasks	
Critical Split		Baseline Split		Project Summary	
Critical Progress		Baseline Milestone		External Milestone	
Task		Milestone		Deadline	
Split		Summary Progress			
Task Progress		Summary			

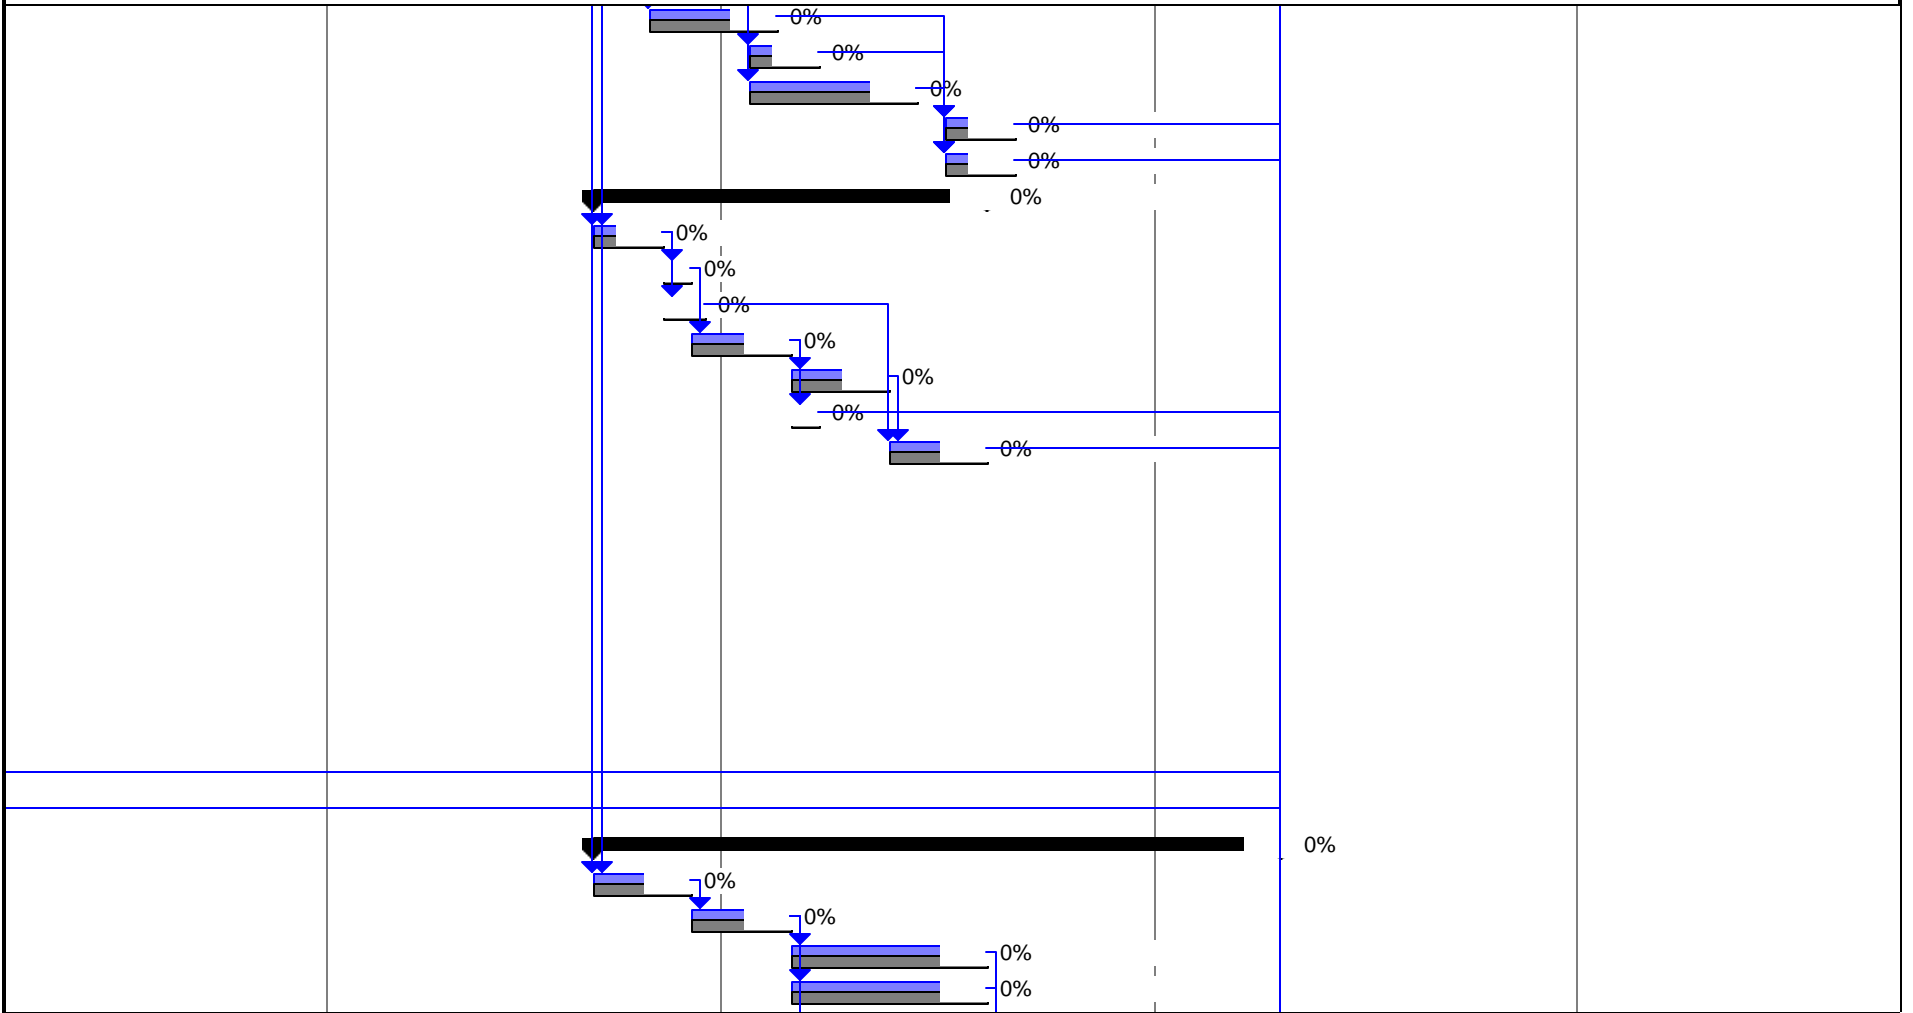

Project: 0201 CS Baseline 20021106
 Date: Sun 11/10/02

Critical		Baseline		External Tasks	
Critical Split		Baseline Split		Project Summary	
Critical Progress		Baseline Milestone		External Milestone	
Task		Milestone		Deadline	
Split		Summary Progress			
Task Progress		Summary			



Project: 0201 CS Baseline 20021106 Date: Sun 11/10/02	Critical		Baseline		External Tasks	
	Critical Split		Baseline Split		Project Summary	
	Critical Progress		Baseline Milestone		External Milestone	
	Task		Milestone		Deadline	
	Split		Summary Progress			
	Task Progress		Summary			
